PRINTED BY: mmurdock65@email.phoenix.edu. Printing is for personal, private use only. No part of this book may be reproduced or transmitted without publisher's prior permission. Violators will be prosecuted.

Given the project network and baseline information below, complete the form to develop a status report for the project at the end of period 4 and the end of period 8. From the data you have collected and computed for periods 4 and 8, what information are you prepared to tell the customer about the status of the project at the end of period 8?

Page 485

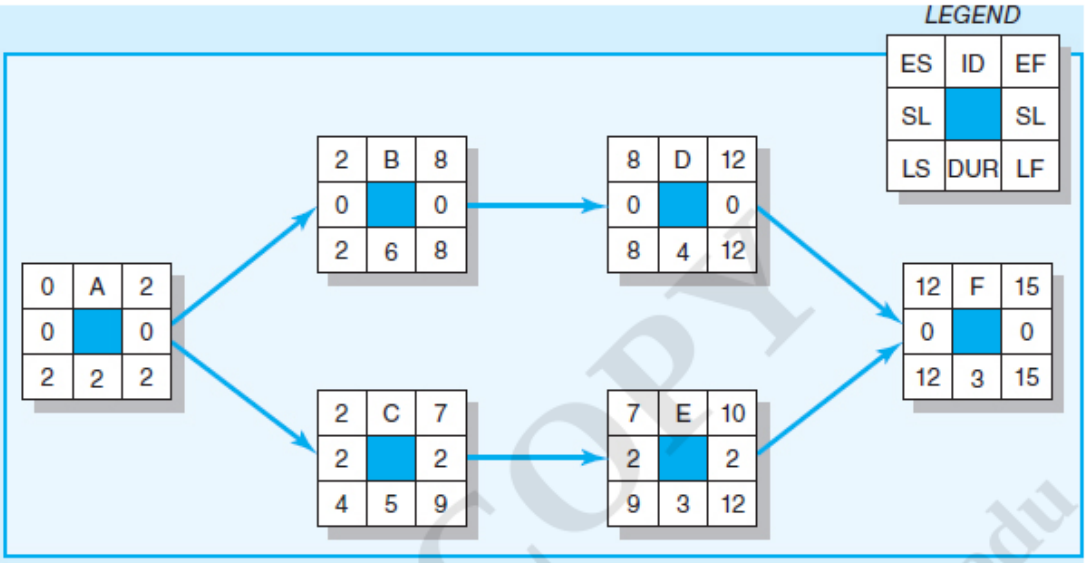

Project baseline (PV) (in $)

Task	DUR	ES	LF	SL	Budget (PV)	0	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15
A	2	0	2	0	400	200	200														
B	6	2	8	0	2400			200	600	200	600	200	600								
C	5	2	9	2	1500			200	400	500	100	300									
D	4	8	12	0	1600									400	400	400	400				
E	3	7	12	2	900								300	400	200						
F	3	12	15	0	600													200	100	300	
Period PV total						200	200	400	1000	700	700	500	900	800	600	400	400	200	100	300	
Cumulative PV total						200	400	800	1800	2500	3200	3700	4600	5400	6000	6400	6800	7000	7100	7400	

End of Period 4

Task	Actual % Complete	EV	AC	PV	CV	SV
A	Finished	—	300	400	—	—
B	50%	—	1000	800	—	—
C	33%	—	500	600	—	—
D	0%	—	0	—	—	—
E	0%	—	—	—	—	—
Cumulative Totals		—	—	—	—	—

Page 486

DO NOT COPY mmurdock65@email.phoenix.edu
